308 309

MEASUREMENT BOOK

Date	Full description, etc, of work	Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Premeasurement recorded on 22/4/13						
I-11	Providing & laying in position plain cement 1:4:8 using 40mm						
		1	×30.0×	$\frac{5.2+5.2}{2}$	×0.15	= 23.40 cum	
		1	×30.0×	$\frac{5.2+5.5}{2}$	×0.15	= 24.07 cum	
		1	×10.0×	$\frac{5.5+6.0}{2}$	×0.15	= 8.62 cum	
		1	×9.0	×4.0	×0.15	= 5.40 cum	
		1	×18.0	×$\frac{2.7+2.7}{2}$	×0.15	= 7.29 cum	
		1	×30.0×	$\frac{6.0+6.0}{2}$	×0.15	= 27.0 cum	
		1	×30.0×	$\frac{6.0+6.0}{2}$	×0.15	= 27.0 cum	
	CE9C 22/4/13 ಸಹಾಯಕ ... ಶೆಟ್ಟಿಹಳ್ಳಿ ಬೃಹತ್ ಬೆಂ...	1	×13.0×	$\frac{6.0+6.0}{2}$	×0.15	= 11.70 cum	
					Limited to	134.48 cum 121.50 cum	Ravi.N.K. 22/4/13

M. A. R. 57 (Rule 116)
Measurement Book

No. B 83001

BR 308/31.8.13

Serial No. 1st & final.

Name of work Providing cc Roads at Chikkasandra colony near Govt School in Shettyhalli Sub-Division Ward no-12 From ...... To ...... Est cost:- 9.9 lakhs

Name of Contractor of nature of Agency... Technical manager (West) KRIDL

Date of commencement of work... No EE/DD/WO/352/12-13 D:- 15/2/13 JC:- 012-11-000069

Date	Full description, etc, of work	Number	Length	Breadth	Depth	Contents	Reference to last Measurement
	2	3	4	5	6	7	8
I-1	Earthwork in surface excavation in ordinary soil for levelling and lowering the ground manually (other than foundation of buildings, culverts, road drains) and removing the excavated stuff to a distance not exceeding 50m & lift upto 1.5m excavated surface leveled & neatly dressed disposed earth to be leveled after breaking. complete as per specifications						
	Qty vide Pg No 83001/2 of this M.B.					283.50 cum 2.69- @ 127=20 Rs - 36061=00 34217 L	
I-2	Earthwork excavation for foundation of buildings culverts water supply sanitary line and electrical conduits						

MEASUREMENT BOOK

Date 1	Full description, etc, of work 2	Number 3	Length 4	Breadth 5	Depth 6	Contents 7	Reference to last Measurement 8
	cfte 29/8/13 ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು		1 × 6.0			= 6.0 m 11.20 @ 130=38	Rs. -1460=00
I-13	conveying the excavated earth to a distance of 2Km with all lead & lifts including loading & unloading Qty vide item no ① + ②	283.50 + 110.06 Limited to tender 236.0				= 393.56 m Limited ~~265.0~~ Rs @ 71=33 Rs	16835- -26035=00
	Ravi.N.K. 29/8/13 Total Amount:- 97279 = 00 10% KRIDL charges:- 97279=00 9661 33=- 9661 33=- 10627 46=00	107 0070=00				Ravi.N.K. 29/8/13	
	certificate 1) certified that Contractor has done the work satisfactorily. 2) certified that Contractor has removed all debries from the spot. 3) certified that there is no due work from contractor side. Ravi.N.K. 29/8/13						

ಹೆಗ್ಗನಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ.
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

M.A.R. 57 (Rule 116)
Measurement Book

No. B 83003

Passed for / Admitted for Rs. 106274=00
Cheque for Rs. 914349=00
Name of work .... From .... To ....
Name of Contractor of nature of Agency ....
Date of commencement of work 148397=00
by adjustment Rs. ....

Accounts Superintendent
Executive Engineer
B.B.M.P. Hegganahalli Division

Date	Full description, etc, of work 2	Number 3	Length 4	Breadth 5	Depth 6	Contents 7	Reference to last Measurement 8

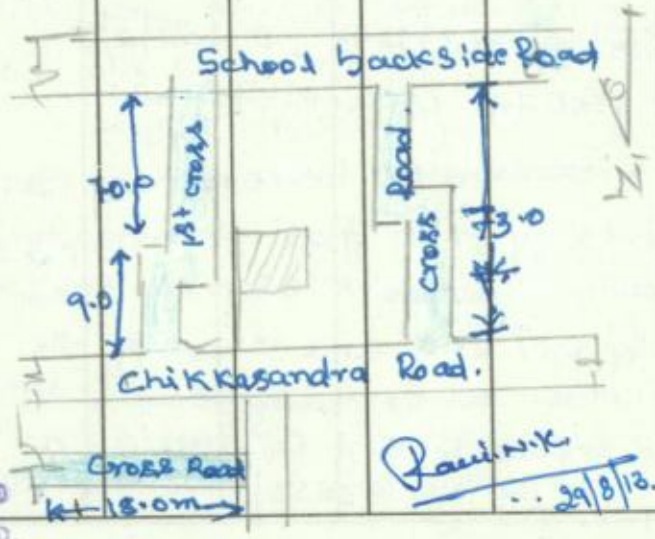

Ravi.N.K. 29/8/13

Ravi.N.K. 29/8/13.

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಹೆಗ್ಗನಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ.
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
